





Ek-Balam Fields



Future Status (July 2026): Completion of the 8"Ø x 8km Akal-B to Ek-A gas pipeline for gas supply to TG and conversion of pipeline 121 from Gas Pipeline to Oil-Gas Pipeline. Decommissioning of pipelines 140, 141, and 147 due to end of service life.


#	Service	Platform Name
1	Drilling Platform	Ek-A
2	Drilling Platform	Ek-A2
3	Accommodation Platform	Ek-A HAB
4	Drilling Platform	Balam-TA
5	Drilling Platform	Balam-TB
6	Drilling Platform	Balam-A
7	Drilling Platform	Balam-TE
8	Drilling Platform	Balam-TD
9	Drilling Platform	Ek-TA
10	Drilling Platform	Ek-TB
11	Drilling Platform	Balam-TA2

#	Pipeline	Service	Age	Length (km)	Diameter (in)	Status
1	L-363	Oil & Gas	New	5.90	20	operating
2	L-368	Oil & Gas	New	0.20	8	operating
3	L-366	Oil & Gas	New	0.17	8	operating
4	L-367	Oil & Gas	New	0.23	8	operating
5	L-364	Oil & Gas	New	3.50	12	operating
6	L-365	Oil & Gas	New	0.20	8	operating
7	L-141	Oil & Gas	Old	4.70	24	operating
8	L-140	Oil & Gas	Old	12.70	24	operating
9	L-147	Oil & Gas	Old	1.20	14	operating
10	L-121	Gas	Old	8.20	20	operating

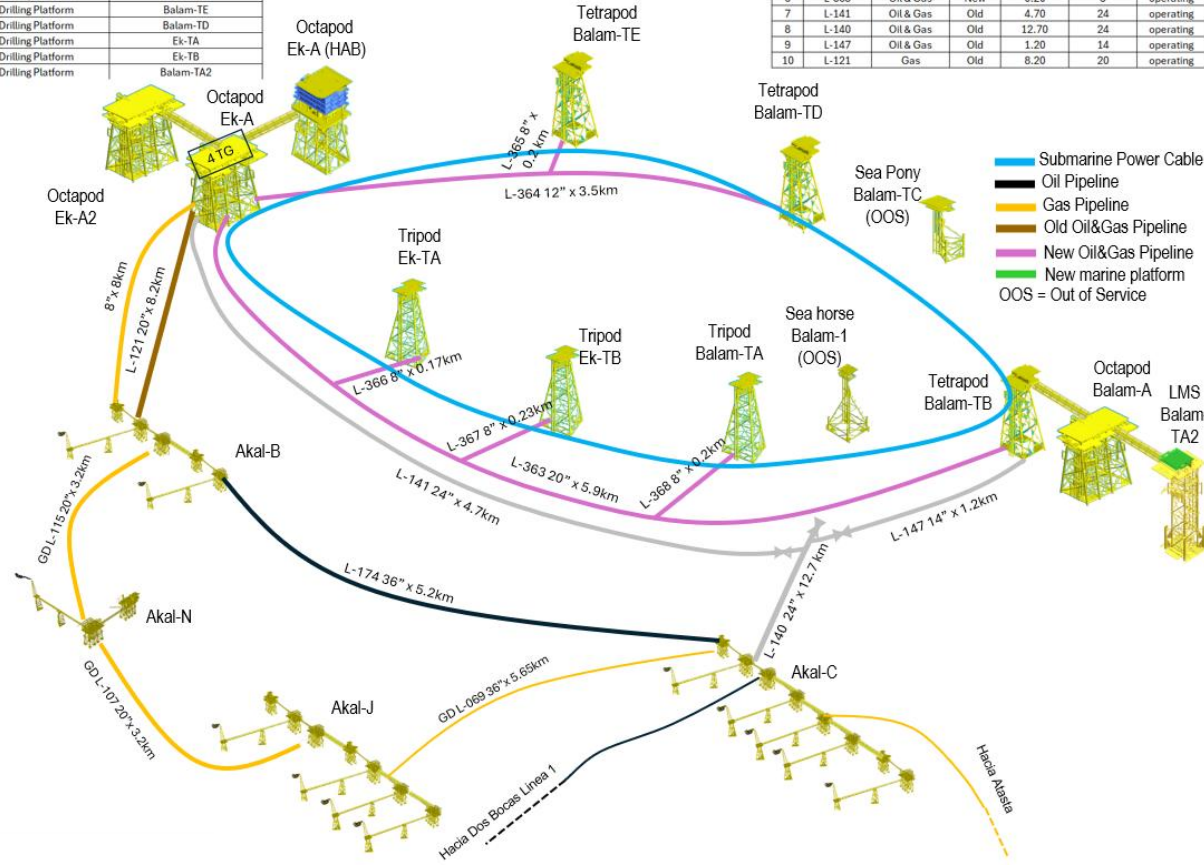




No.	Offshore Platform	Installation Date	Type	Service	Water Depth (m)	Number of wells	Wells
1	Ek-A	2018	Octapod	Drilling	51	6	Ek-11, Ek-27, Ek-31, Ek-33, Ek-56, Ek-101
2	Balam-TB	2017	Tetrapod	Drilling	47.9	4	Balam-47, Balam-63, Balam-67, Balam-83
3	Balam-A	2014	Octapod	Drilling	47.9	6	Balam-32, Balam-41, Balam-42, Balam-61, Balam-85, Balam-93
4	Ek-A2	2018	Octapod	Drilling	51	7	Ek-14, Ek-29, Ek-32, Ek-47, Ek-53, Ek-57, Ek-69
5	Ek-TA	1996	Tripod	Drilling	49.9	5	Ek-9, Ek-17, Ek-21, Ek-25, Ek-37
6	Balam-TE	2020	Tetrapod	Drilling	51.2	5	Balam-71, Balam-75, Balam-91, Ek-35H, Ek-55
7	Balam-TA	2021	Tripod	Drilling	48	2	Balam-2, Balam-22
8	Balam-TA2	2022	Tetrapod (Lightweight Marine Structure)	Drilling	47.9	2	Balam-5, Balam-87
9	Ek-TB	1996	Tripod	Drilling	49.1	2	Ek-41, Ek-63
10	Balam-TD	2005	Tetrapod	Drilling	50.3	1	Balam-3
11	Ek-A Habitacional	2018	Octapod	Accomodation	51	0	None

01.- Ek-A Type of Structure: Octapod / Year of Installation: 2018 / Number of Wells: 6

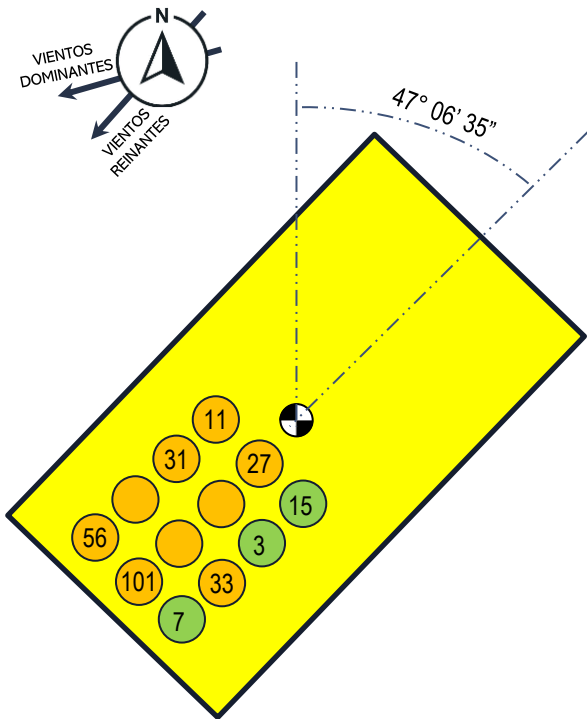

Ek-A	UTM COORDINATES		Type	Drilling Start Date	Drilling Finish Date	Total Depth (m)	Vertical Depth (m)
	X	Y					
Center of Structure	604,929.49	2,157,272.55	---	---	---	---	---
Well Ek-11	604,923.39	2,157,269.98	Deviated	14-May-1993	01-Aug-1993	4874	4671
Well Ek-27 DES (Development)	604,925.31	2,157,268.05	Vertical	02-Jul-2022	13-Oct-2022	5035	4223
Well Ek-31	604,921.94	2,157,267.79	Deviated	03-Apr-1991	03-Dic-1991	5158	4755
Well Ek-33 INY	604,922.86	2,157,261.75	Deviated	17-Mar-1994	15-Aug-1994	4884	4632
Well Ek-56	604,916.81	2,157,263.41	Directional	27-Jul-2012	08-Oct-2012	3133	2981
Well Ek-101	604,918.74	2,157,261.48	Vertical	01-Mar-1990	17-Ene-1991	4607	4607

02. - BALAM-TB Type of Structure: Tetrapod / Year of Installation: 2017 / Number of Wells: 4

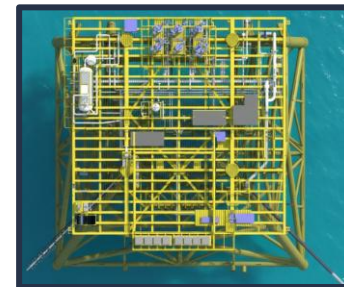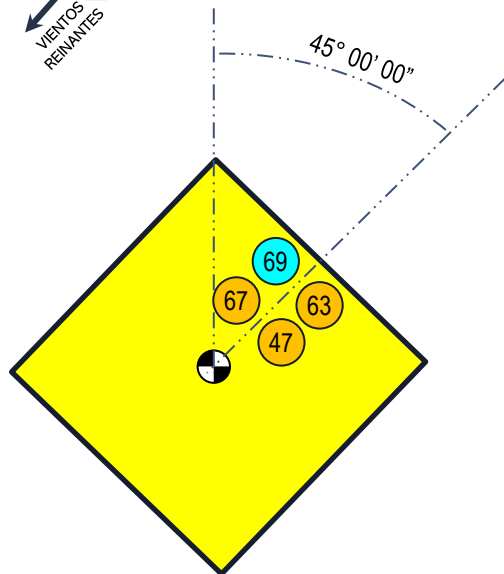

Balam-TB	UTM COORDINATES		Type	Drilling Start Date	Drilling Finish Date	Total Depth (m)	Vertical Depth (m)
	X	Y					
Center of Structure	609,952.53	2,154,716.54	---	---	---	---	---
Well Balam-47 DES (Development)	609,958.52	2,154,718.62	Horizontal	12-May-2018	10-Ago-2018	5149	4430
Well Balam-63 DES (Development)	609,960.77	2,154,720.86	Directional	27-Oct-2018	23-Jan-2019	4621	4508
Well Balam-69 INY (Water Injector)	609,958.43	2,154,722.85	Directional	26-Feb-2019	26-May-2019	5340	4835
Well Balam-67 DES (Development)	609,958.74	2,154,722.41	Directional	28-Jan-2020	26-Apr-2020	5296	4532



Occupied Active



Available



Occupied Inactive




Not Available




Water Injector

03.- Balam-A Type of Structure: Octapod / Year of Installation: 2014 / Number of Wells: 6

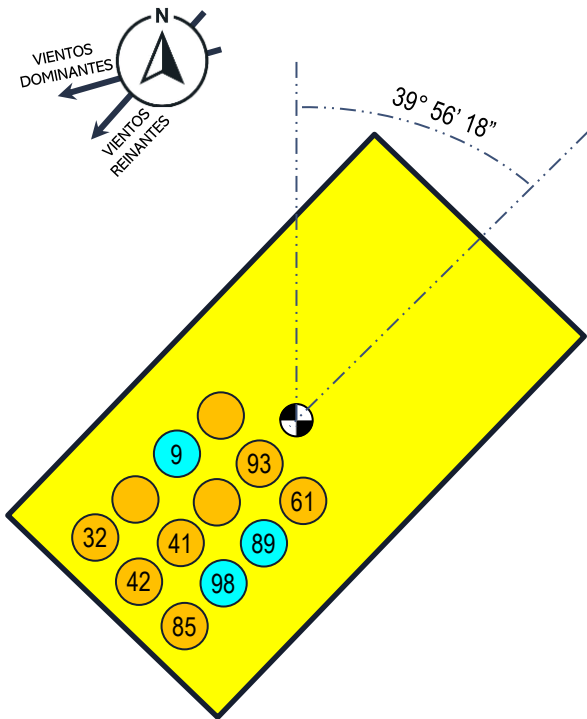


Balam-A	UTM COORDINATES		Type	Drilling Start Date	Drilling Finish Date	Total Depth (m)	Vertical Depth (m)
	X	Y					
Center of Structure	610,033.85	2,154,602.36	---	---	---	---	---
Well Balam-32 DES (Development)	610,021.61	2,154,592.48	Horizontal	14-Jul-2022	25-Nov-2022	5174	4512
Well Balam-42 DES (Development)	610,023.72	2,154,590.75	Directional J	26-Jun-2019	23-Nov-2019	5302	4983
Well Balam-85 DES (Development)	610,025.84	2,154,589.02	Directional	13-Mar-2020	16-Sep-2020	5034	4681
Well Balam-98 INY (Water Injector)	610,027.79	2,154,591.43	Directional	05-Jun-2021	10-Oct-2021	5130	4532
Well Balam-41 DES (Development)	610,025.68	2,154,593.15	Directional	01-Mar-2023	04-Jun-2023	4900	4594
Well Balam-89 INY (Water Injector)	610,029.75	2,154,593.83	Horizontal	16-Ago-2023	26-Nov-2023	5800	4806
Well Balam-9 INY (Water Injector)	610,026.27	2,154,597.35	Directional J	30-Nov-2018	07-May-2019	5156	4755
Well Balam-61 DES (Development)	610,031.71	2,154,596.23	Directional	22-Nov-2020	09-Apr-2021	5101	4483
Well Balam-93 DES (Development)	610,029.60	2,154,597.95	Directional	01-Dec-2021	09-Mar-2022	4826	4463

04.- Ek-A2 Type of Structure: Octapod / Year of Installation: 2018 / Number of Wells: 7

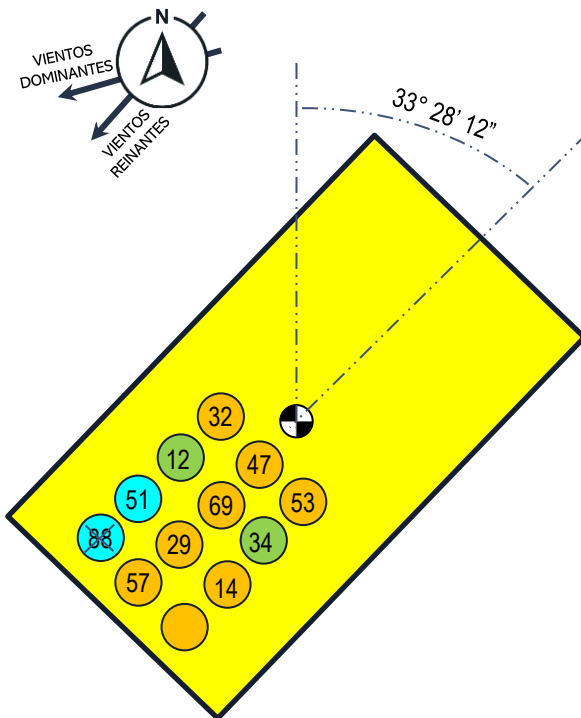

Ek-A2	UTM COORDINATES		Type	Drilling Start Date	Drilling Finish Date	Total Depth (m)	Vertical Depth (m)
	X	Y					
Center of Structure	604,791.19	2,157,360.12	---	---	---	---	---
Well Ek-57 DES (Development)	604,782.27	2,157,347.50	Directional	04-May-2023	10-Jul-2023	5403	4725
Well Ek-29 DES (Development)	604,783.98	2,157,350.07	Horizontal	07-Jul-2022	30-Sep-2022	5443	4608
Well Ek-14 DES (Development)	604,786.25	2,157,348.57	Directional	14-Mar-2021	20-May-2021	5110	4225
Well Ek-69 DES (Development)	604,785.70	2,157,352.65	Horizontal	12-Nov-2022	31-Mar-2023	5667	4654
Well Ek-32 DES (Development)	604,785.15	2,157,356.74	Directional J	09-Aug-2019	22-Dec-2019	4680	4565
Well Ek-47 DES	604,787.42	2,157,355.23	Directional	28-Jun-2020	18-Sep-2020	5066	4255
Well Ek-53 DES	604,789.69	2,157,353.73	Directional J	08-Dec-2021	07-Feb-2022	4467	4264

05.- Ek-TA Type of Structure: Tripod / Year of Installation: 1996 / Number of Wells: 5



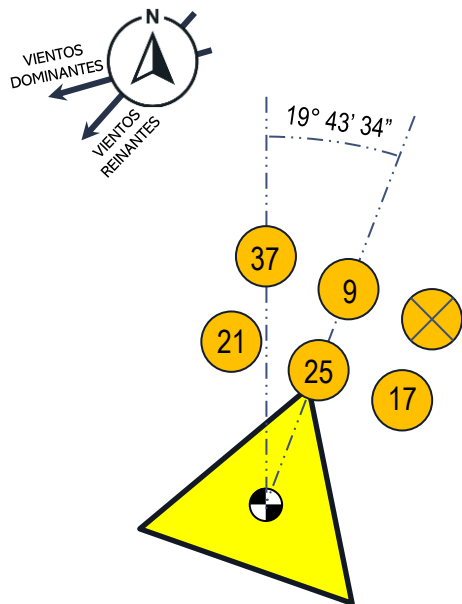


Ek-TA	UTM COORDINATES		Type	Drilling Start Date	Drilling Finish Date	Total Depth (m)	Vertical Depth (m)
	X	Y					
Center of Structure	606,152.50	2,156,600.00	---	---	---	---	---
Well Ek-37 DES (Development)	606,152.83	2,156,605.04	Directional J	29-Jul-2019	20-Oct-2019	4520	4261
Well Ek-9	606,154.49	2,156,605.43	Horizontal	02-Apr-2014	12-May-2015	--	--
Well Ek-21IN	606,151.86	2,156,604.27	Directional	28-May-1993	26-Jul-1993	4852	4699
Well Ek-25	606,154.35	2,156,603.51	Directional	30-Jan-1994	11-Apr-1994	4380	4298
Well Ek-17 DES (Development)	606,155.18	2,156,603.29	Horizontal	07-Dec-2018	30-Apr-2019	4912	4416

06. - BALAM-TE Type of Structure: Tetrapod / Year of Installation: 2020 / Number of Wells: 5



3° 02' 35"

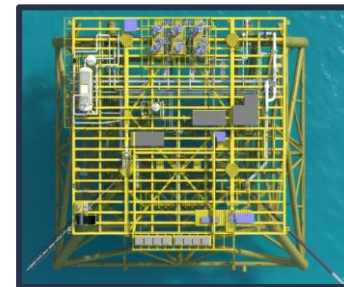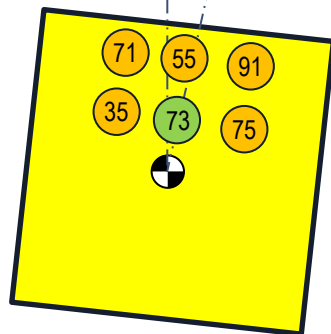

Balam-TE	UTM COORDINATES		Type	Drilling Start Date	Drilling Finish Date	Total Depth (m)	Vertical Depth (m)
	X	Y					
Center of Structure	606,840.50	2,158,066.56	---	---	---	---	---
Well Balam 71 (Development)	606,837.62	2,158,075.94	Directional	26-Jul-1993	14-Feb-1994	3643	3379
Well Ek 55 (Development)	606,840.39	2,158,075.74	Deviated	31-Dic-2008	26-Mar-2009	3707	3081.3
Well Balam 91 (Development)	606,843.03	2,158,075.60	Deviated	05-Mar-1993	10-Jul-1993	4611	4572
Well Ek 35H	606,837.31	2,158,072.97	Horizontal	23-Aug-2009	07-Nov-2009	3497	3004
Well Balam 75H	606,842.85	2,158,072.56	Horizontal	21-Aug-2013	02-Aug-2014	4845	4476



Occupied Active



Available



Occupied Inactive




Not Available





Water Injector

07.- BALAM-TA Type of Structure: Tripod / Year of Installation: 2021 / Number of Wells: 2

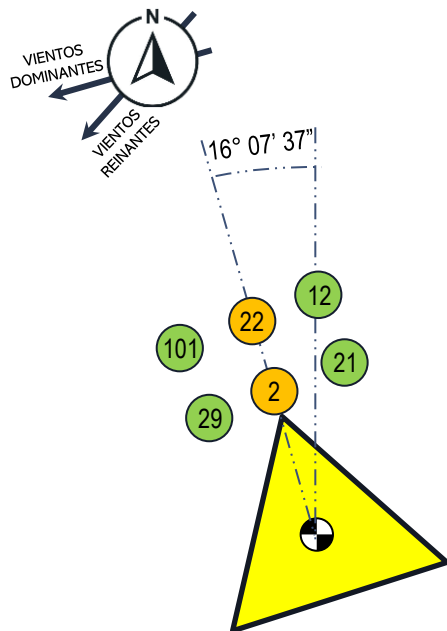


Balam-TA	UTM COORDINATES		Type	Drilling Start Date	Drilling Finish Date	Total Depth (m)	Vertical Depth (m)
	X	Y					
Center of Structure	608,504.52	2,155,269.54	---	---	---	---	---
Well Balam-22H DES (Development)	608,502.79	2,155,274.62	Horizontal	10-Jan-2020	18-Mar-2020	5140	---
Well Balam-2H DES (Development)	608,503.24	2,155,272.43	Horizontal	27-Apr-2021	30-Aug-2021	5119	4457

08.- BALAM-TA2 Type of Structure: LMS (Tetrapod) / Year of Installation: 2022 / Number of Wells: 2

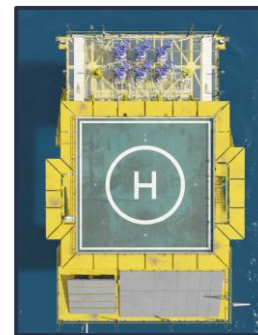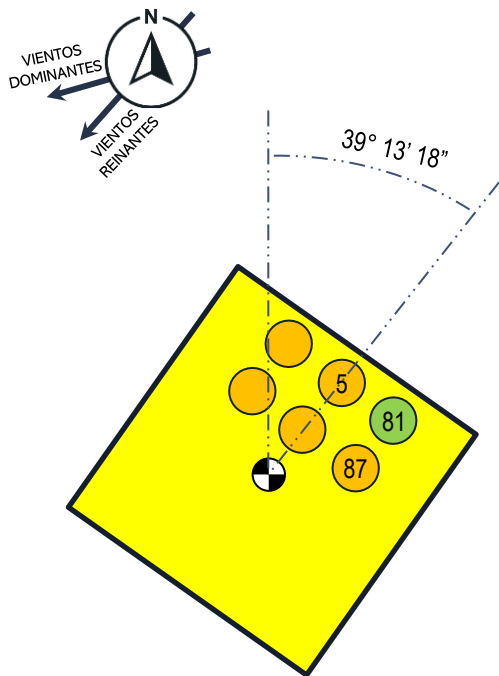

Balam-TA2	UTM COORDINATES		Type	Drilling Start Date	Drilling Finish Date	Total Depth (m)	Vertical Depth (m)
	X	Y					
Center of Structure	610,090.34	2,154,565.33	---	---	---	---	---
Well Balam-5 DES (Development)	610,095.67	2,154,572.80	Directional	01-Aug-2022	03-Oct-2022	5660	4577
Well Balam-87 DES (Development)	610,095.78	2,154,568.78	Directional	16-Feb-2026	30-Abr-2023	5180	4480

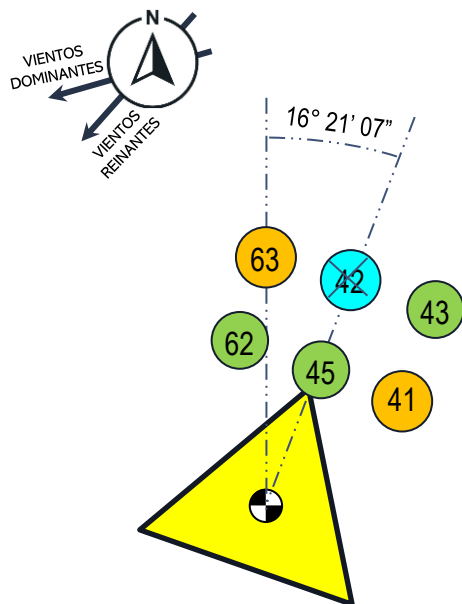

Ek-TB	UTM COORDINATES		Type	Drilling Start Date	Drilling Finish Date	Total Depth (m)	Vertical Depth (m)
	X	Y					
Center of Structure	607,325.51	2,155,847.54	---	---	---	---	---
Well Ek 63 DES (Development)	607,325.84	2,155,852.03	Deviated	11-Apr-1993	17-Jul-1993	4937	4790
Well Ek-41 (Development)	607,328.19	2,155,850.28	Directional	10-Nov-2013	18-Feb-2014	---	---



Occupied Active



Available



Occupied Inactive



Not Available





Water Injector


10.- BALAM-TD Type of Structure: Tetrapod / Year of Installation: 2005 / Number of Wells: 1



10° 00' 05"

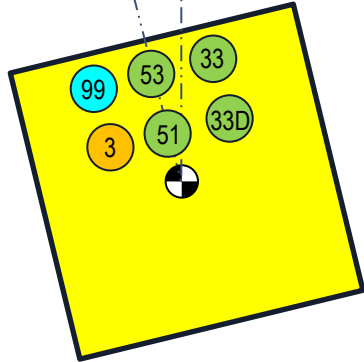

Balam-3

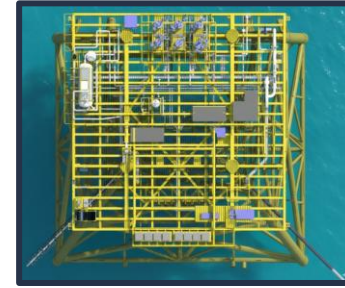

Balam-TD	UTM COORDINATES		Type	Drilling Start Date	Drilling Finish Date	Total Depth (m)	Vertical Depth (m)
	X	Y					
Center of Structure	608,116.51	2,157,259.55	---	---	---	---	---
Well Balam 99 INY (Water Injector)	608,111.08	2,157,268.48	Directional J	08-Aug-2017	31-Oct-2017	5204	4829
Well Balam 3H DES (Development)	608,111.64	2,157,265.30	Horizontal	25-Sep-2018	18-Dec-2018	5386	4418



Occupied Active



Available



Occupied Inactive



Not Available



Water Injector
